


MINNEAPOLIS

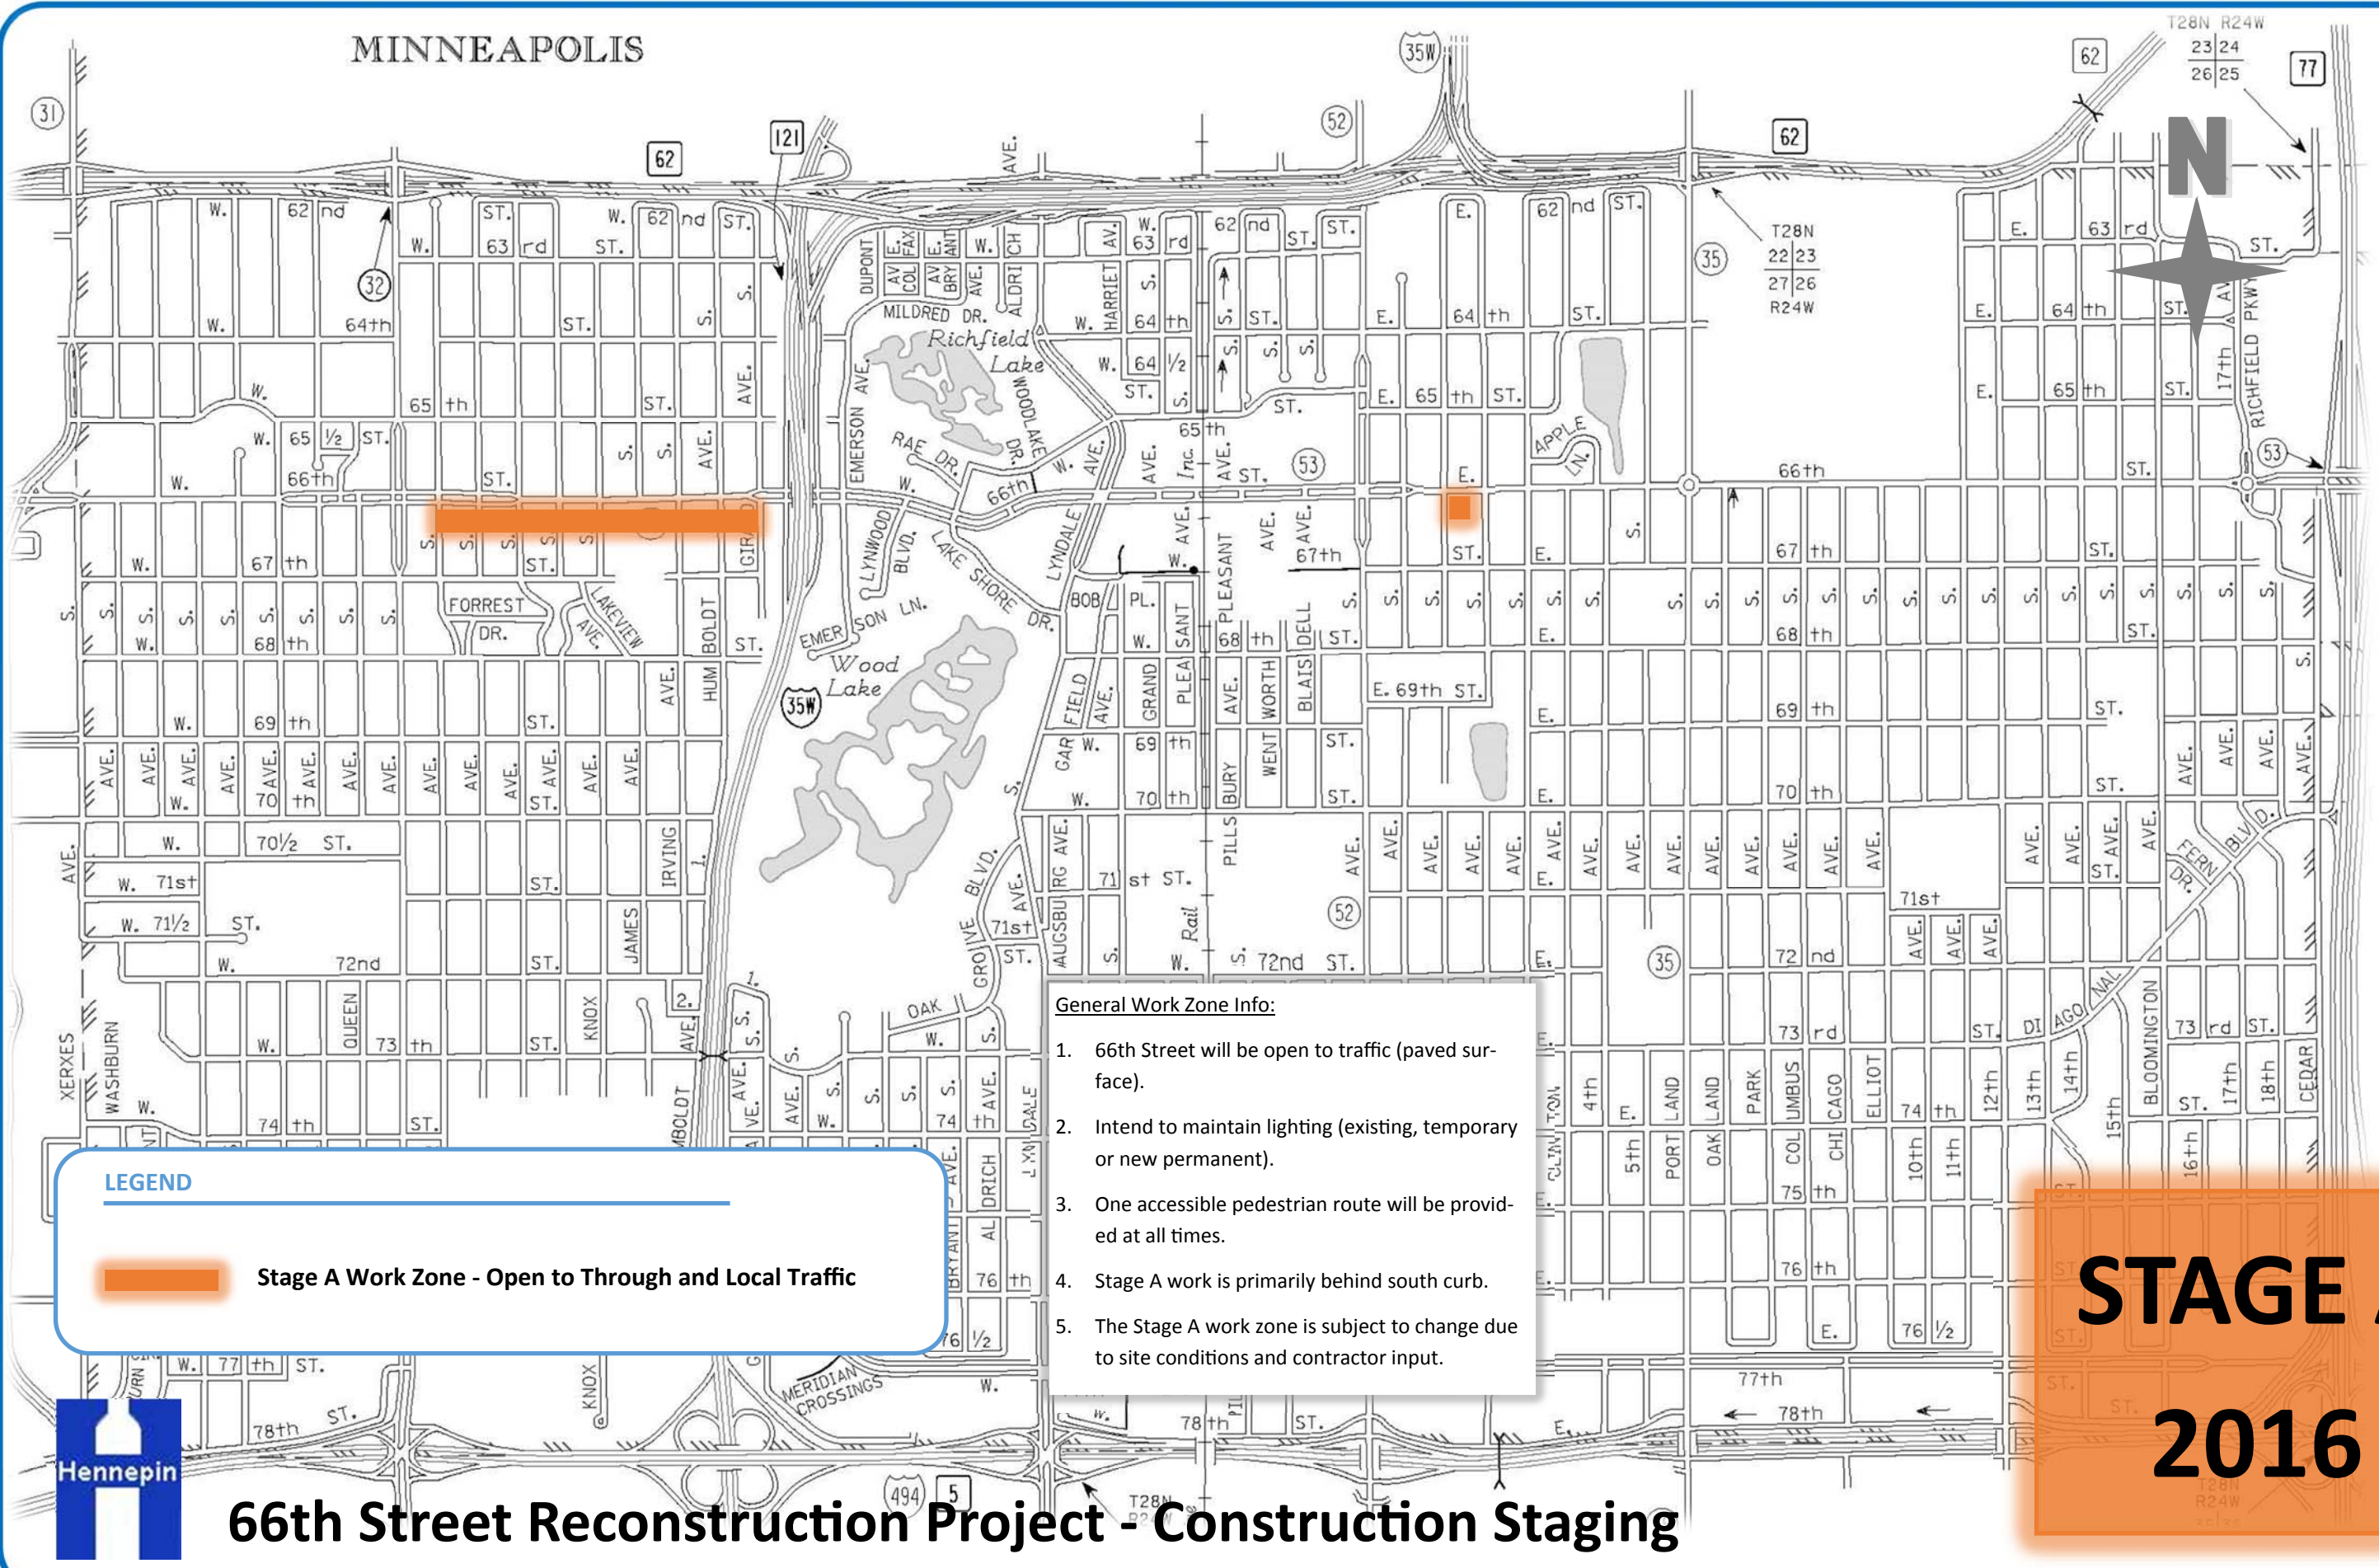

General Work Zone Info:

1. 66th Street will be open to traffic (paved surface).
2. Intend to maintain lighting (existing, temporary or new permanent).
3. One accessible pedestrian route will be provided at all times.
4. Stage A work is primarily behind south curb.
5. The Stage A work zone is subject to change due to site conditions and contractor input.

LEGEND


 Stage A Work Zone - Open to Through and Local Traffic

STAGE A
2016



66th Street Reconstruction Project - Construction Staging

MINNEAPOLIS

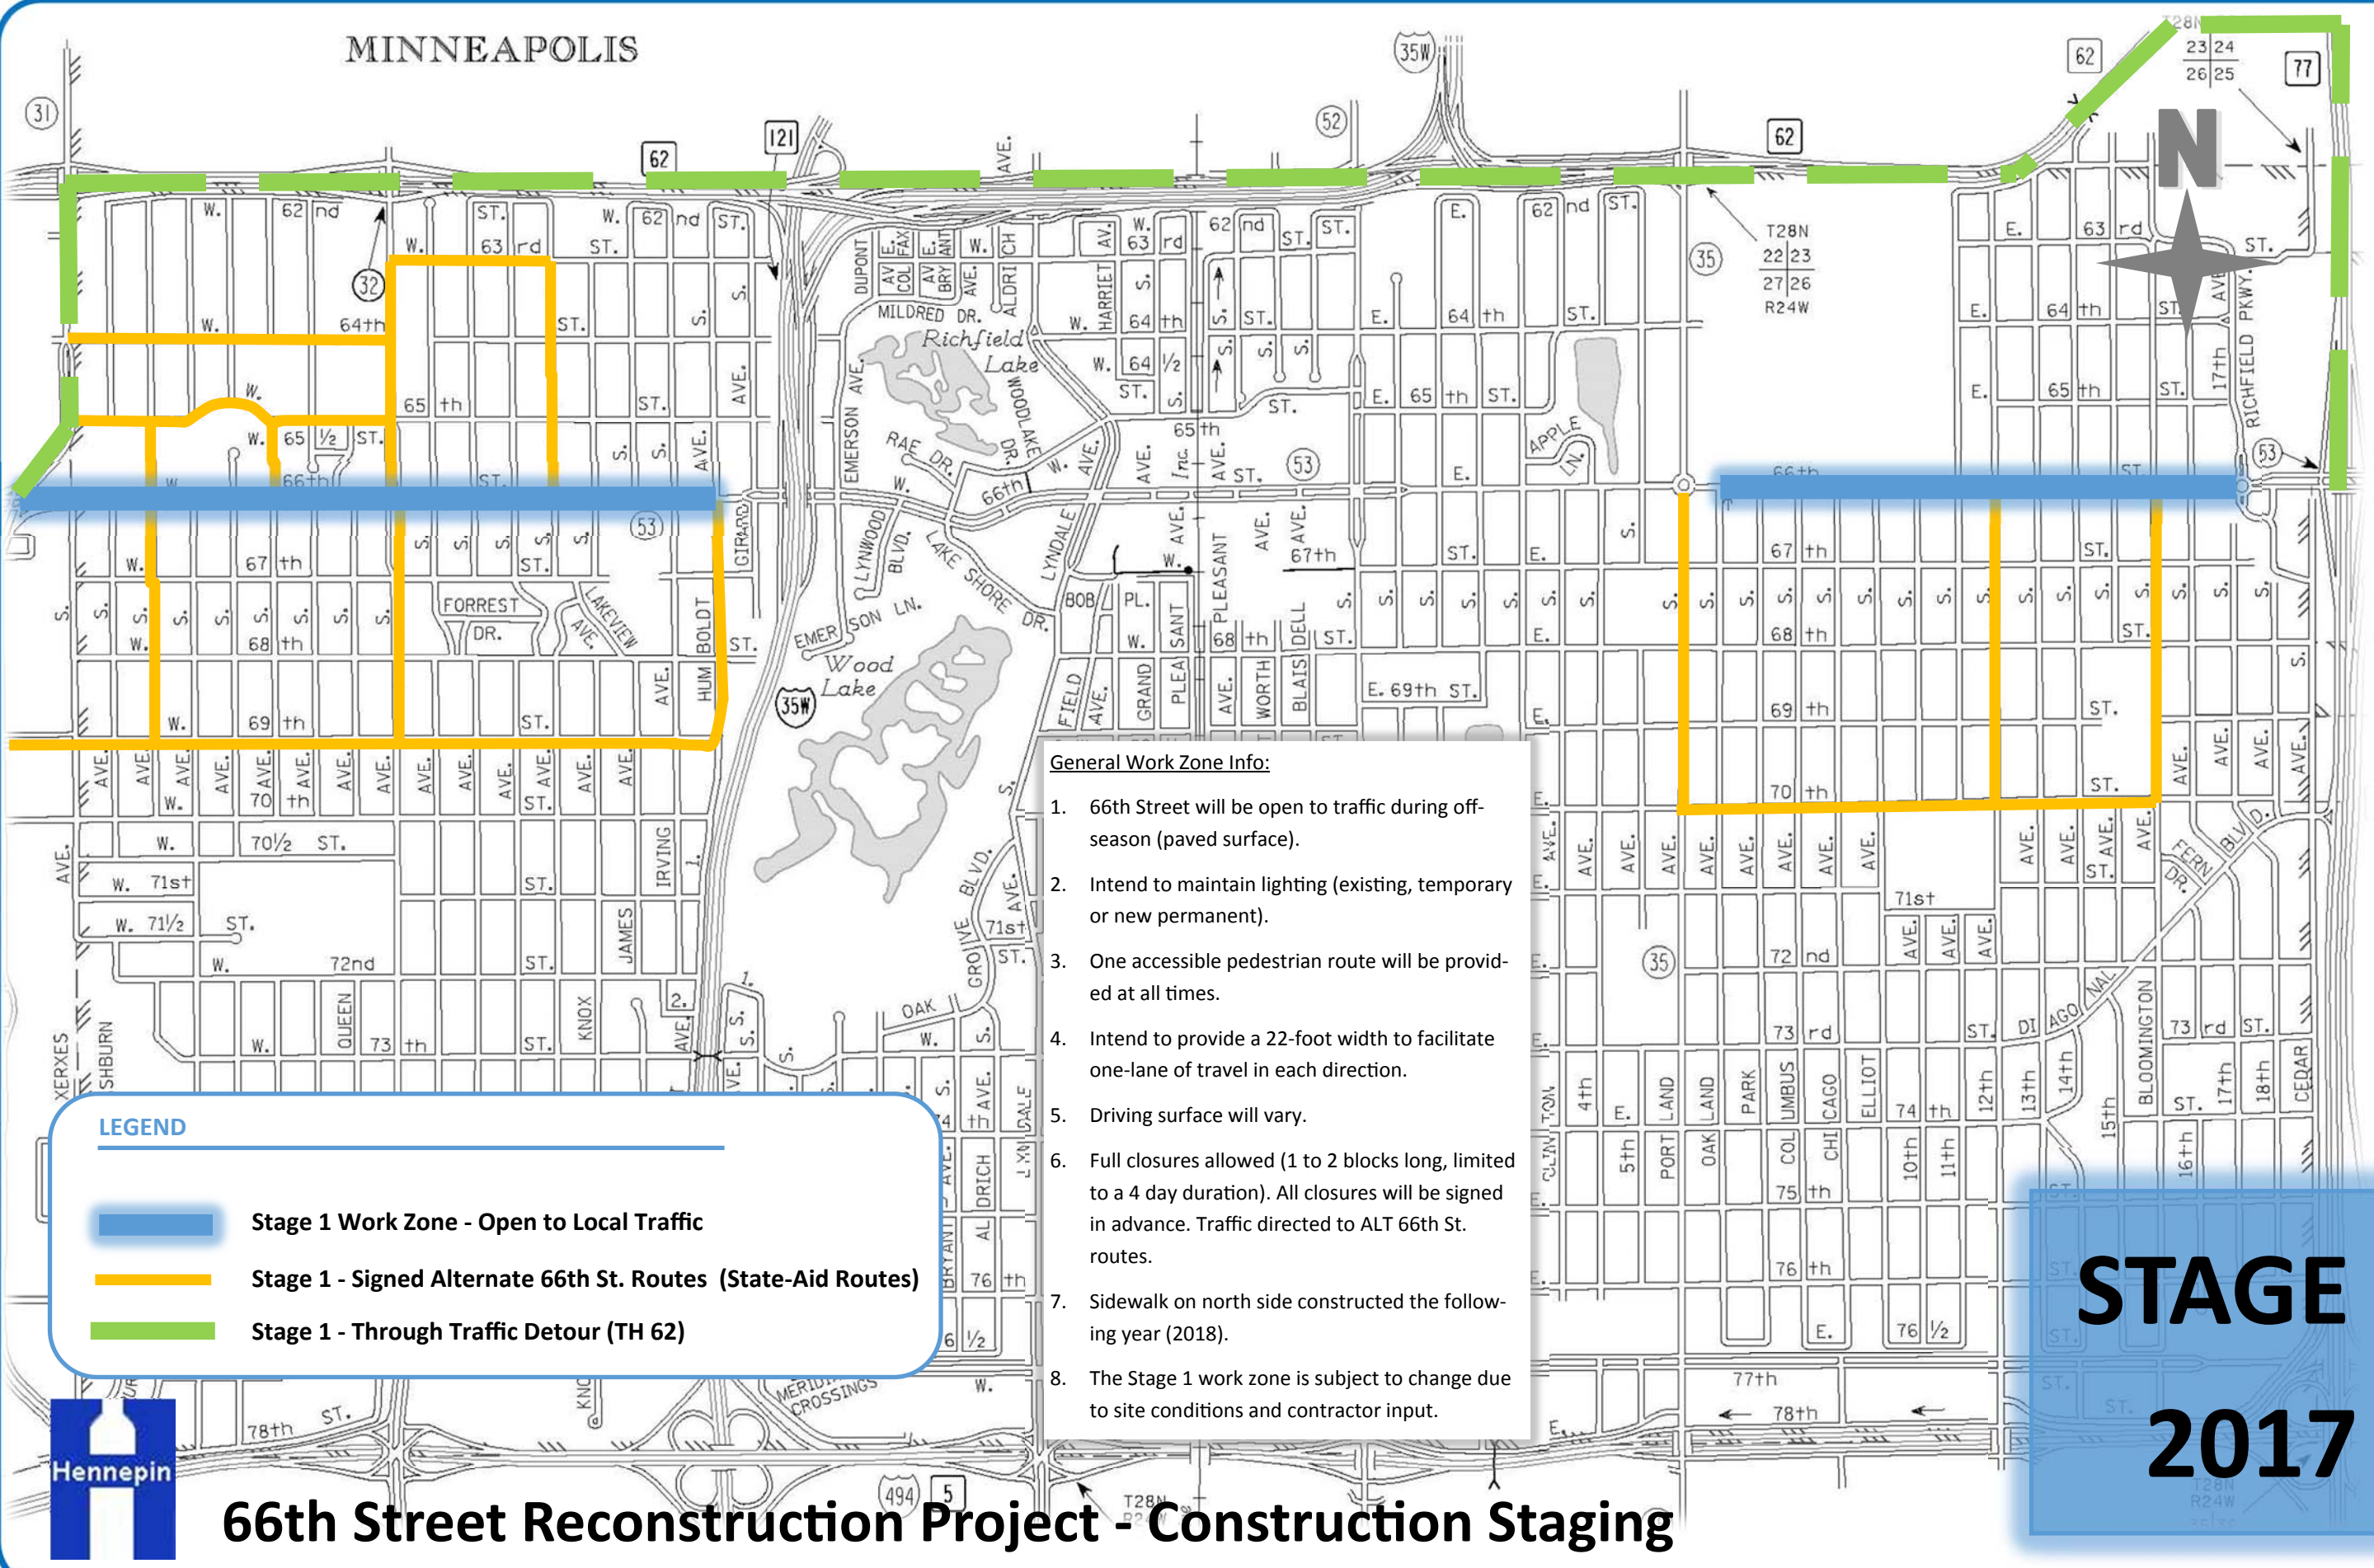

General Work Zone Info:

1. 66th Street will be open to traffic during off-season (paved surface).
2. Intend to maintain lighting (existing, temporary or new permanent).
3. One accessible pedestrian route will be provided at all times.
4. Intend to provide a 22-foot width to facilitate one-lane of travel in each direction.
5. Driving surface will vary.
6. Full closures allowed (1 to 2 blocks long, limited to a 4 day duration). All closures will be signed in advance. Traffic directed to ALT 66th St. routes.
7. Sidewalk on north side constructed the following year (2018).
8. The Stage 1 work zone is subject to change due to site conditions and contractor input.

LEGEND


- Stage 1 Work Zone - Open to Local Traffic
- Stage 1 - Signed Alternate 66th St. Routes (State-Aid Routes)
- Stage 1 - Through Traffic Detour (TH 62)

STAGE 1
2017



66th Street Reconstruction Project - Construction Staging

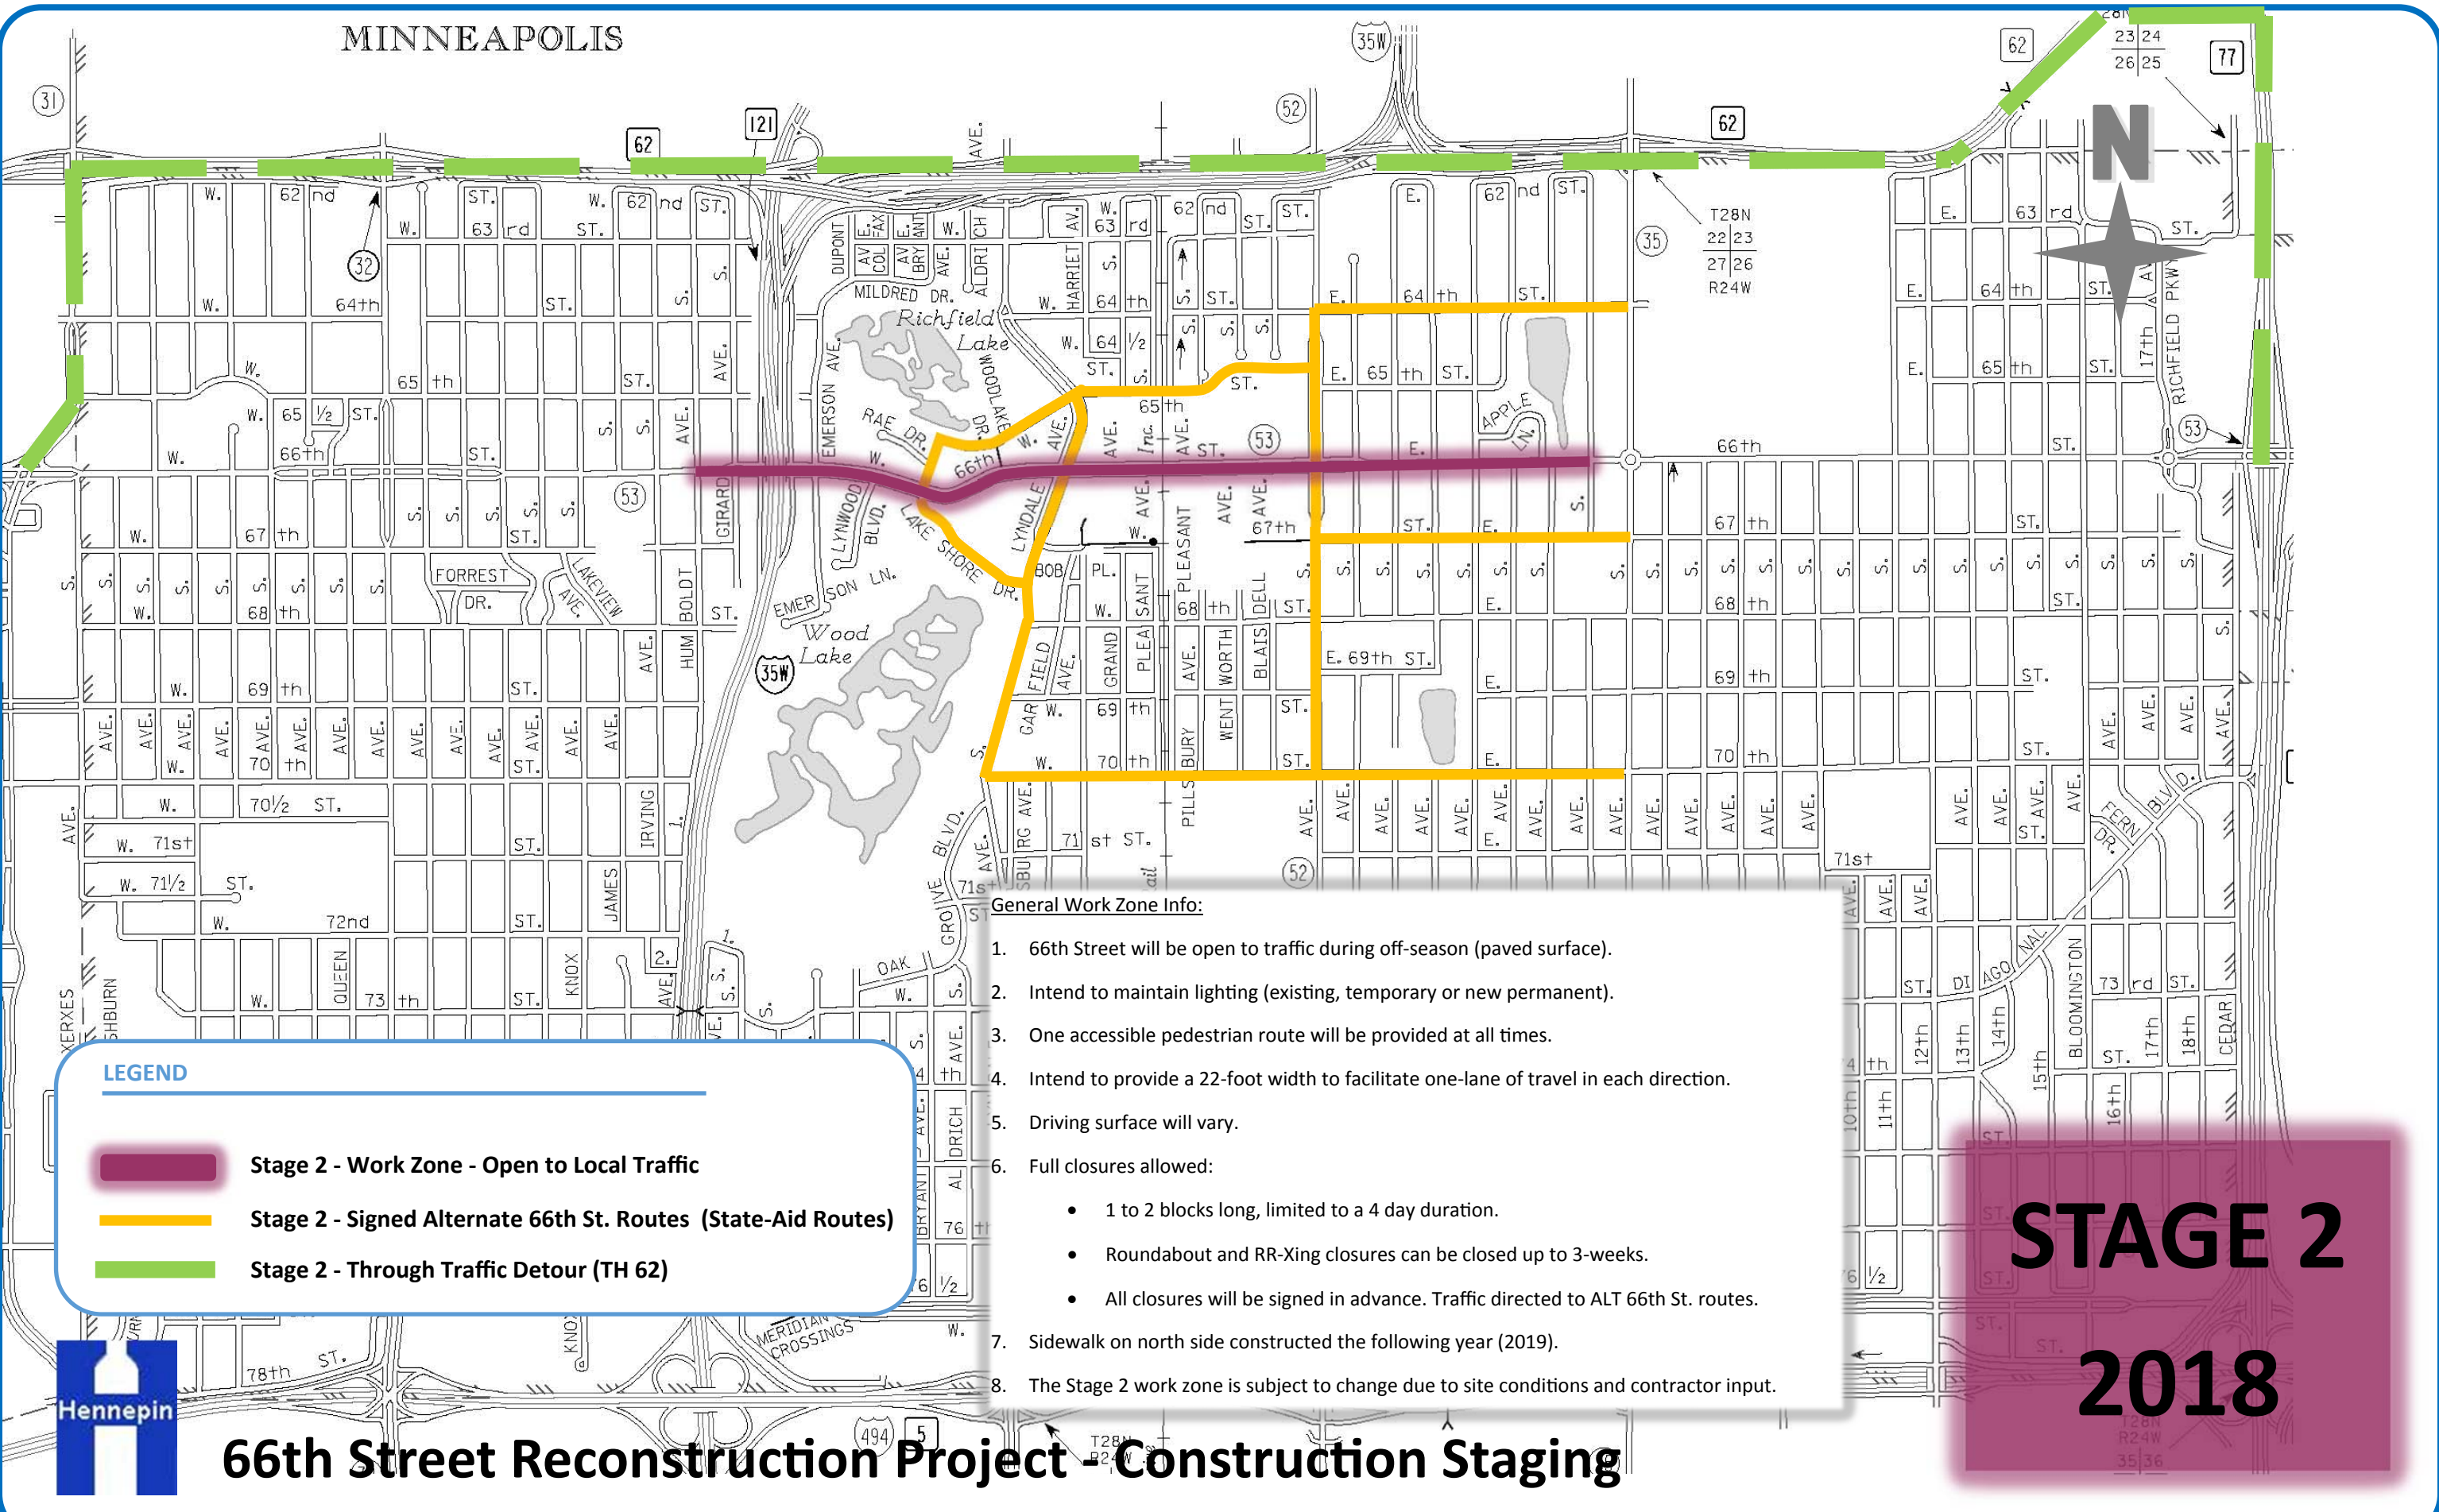


MINNEAPOLIS



General Work Zone Info:

1. 66th Street will be open to traffic during off-season (paved surface).
2. Intend to maintain lighting (existing, temporary or new permanent).
3. One accessible pedestrian route will be provided at all times.
4. Intend to provide a 22-foot width to facilitate one-lane of travel in each direction.
5. Driving surface will vary.
6. Full closures allowed:
 - 1 to 2 blocks long, limited to a 4 day duration.
 - Roundabout and RR-Xing closures can be closed up to 3-weeks.
 - All closures will be signed in advance. Traffic directed to ALT 66th St. routes.
7. Sidewalk on north side constructed the following year (2019).
8. The Stage 2 work zone is subject to change due to site conditions and contractor input.

LEGEND

-  Stage 2 - Work Zone - Open to Local Traffic
-  Stage 2 - Signed Alternate 66th St. Routes (State-Aid Routes)
-  Stage 2 - Through Traffic Detour (TH 62)



66th Street Reconstruction Project - Construction Staging

STAGE 2
2018
